

Station name	KPC - L (OLD)
People present	APA, CLAN, PHO, OEW + Kiddi & Bjarni
Purpose	Maintenance / installation / take-down / quick visit / emergency
Date	28/5- 2022

Notes:

Quick Trimble R8 on abl. box
98 cm above mid-parameter
65 cm below base of Rotunil's

AWS to do list		Check after maintenance		
Part	Part shipped (Y/N)	Shipped part number	Part number upon departure.	
Radiometer				Clean? ☒ Y/N
Ablation hose assembly				No air in hose and bladder half full? Y/N under snow
Iridium modem IMEI number				
Inclinometer/compass		Attached to the radiometer? Y/N		
Satellite antenna				
Wind sensor		Black box pointing toward the radiometer (i.e. along the boom)? ☒ Y/N		
Temperature / humidity assembly		Fan spins? ☒ Y/N Sounds OK? ☒ Y/N		
HygroClip in T/hum assembly		NB: could have a 40 °C offset		
Sonic ranger on AWS		Old sensor with new membrane? Y/N 203		
Sonic ranger on stake(s)		Old sensor with new membrane? Y/N NB: make sure not being buried next winter fallen over		
Thermistor string		no access		
Solar panel		Clean? ☒ Y/N NB: is not effective when partially covered		
GPS antenna		At top of logger enclosure? ☒ Y/N		
Data logger		☒ CR1000 or CR1000X?		
Multiplexer		Clicking during measurement cycle? Y/N		
Logger enclosure		Replaced (including everything inside)? ☒ Y/N New desiccant bags? ☒ Y/N		
Battery box		New box? Y/N New desiccant bags? Y/N NO see		
Stakes		New one(s) drilled in? Y/N Length of new stake(s) 8 m? Y/N Bottom plugged to reduce melt-in? Y/N fallen over		
Tripod		New tripod? ☒ Y/N New sensor boom? ☒ Y/N		

Metadata maintenance

Arrival


Departure

Time difference between logger clock and UTC ($\pm$ mm:ss)		-00:57
Download data to PC and/or change CF Card (wait for green light)	Y / N	(Y) / N
Name of logger program		promice2015e
Screen dump of values in fast scan mode	Y / N	Y / N
Photos of tripod, sensors, logger box wiring etc. (more is better)	Y / N	(Y) / N
Mast tilt towards radiometer (- if tilting towards anemometer)	°	°
Mast tilt across boom looking from radiometer (- if clockwise)	°	°
Boom direction relative to north	° true/magn.	° true/magn.
Box on wind sensor exactly towards mast? If not, measure.	Y / N	(Y) / N
Radiometer exactly aligned with inclinometer? If not, measure.	Y / N	(Y) / N
Temperature / humidity height (bottom of casing – surface)	cm	183 cm
Stake assembly standing?	Y / N / sort of	(Y) / N / sort of
Free length of stake (if 3: outer, holding boom with sonic ranger)	cm	cm
Free length of stake 2 (if 3: middle)	cm	cm
Free length of stake 3 (if 3: outer, without sonic ranger)	cm	cm
Height of ablation bladder fluid level above the ice surface	cm	cm
Vertical difference in surface height (at station – at hose) (approx.)	cm	cm
Length of thermistor string on surface from surface marking	cm	cm
Apparent damage to sensors? If yes, which?	Y / N	Y / N

Notes:

Robotics base
is 183 cm above snow

Snow depth
~ 80 cm $\pm$ 20 cm

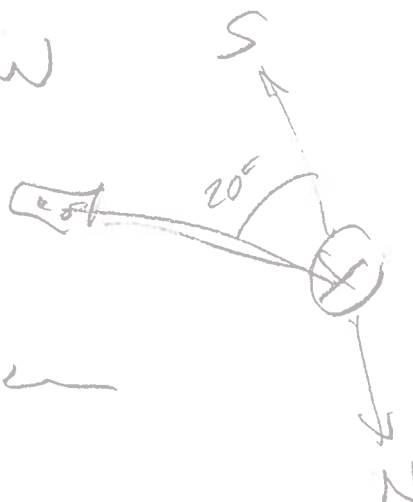

Must-do at next visit:

departing 17:39
