

Station name	KPC - V (OLD)
People present	APA, CLAN, PHO, OEW + Kiddi & Bjarni
Purpose	Maintenance / installation / take-down / quick visit / emergency
Date	28/5-2022

Notes:

GNSS Trunk 18 - 15 min Roving time
 From ~~station~~ centre to hygromclip mount centre: 168 cm (along mast)
 GNSS boom " " upper boom: 185 cm + 33 cm to wind axis
 " " atm press. sensor inside box: 35 cm

AWS to do list		Check after maintenance		
Part	Part shipped (Y/N)	Shipped part number	Part number upon departure.	
Radiometer				Clean? ☒ Y/N
Ablation hose assembly				No air in hose and bladder half full? Y/N NONE
Iridium modem IMEI number			8319330	
Inclinometer/compass		Attached to the radiometer? Y/N		
Satellite antenna				
Wind sensor		Black box pointing toward the radiometer (i.e. along the boom)? Y/N		
Temperature / humidity assembly		Fan spins? Y/N Sounds OK? ☒ Y/N		
HygroClip in T/hum assembly		NB: could have a 40 °C offset Not changed.		
Sonic ranger on AWS		Old sensor with new membrane? Y/N 195 cm to snow surf 4.7 snow depth		
Sonic ranger on stake(s)		Old sensor with new membrane? Y/N NB: make sure not being buried next winter 113 cm to snow 48 cm snow depth		
Thermistor string		under snow		
Solar panel		Clean? ☒ Y/N NB: is not effective when partially covered		
GPS antenna		At top of logger enclosure? ☒ Y/N		
Data logger		CR1000 or CR1000X?		
Multiplexer		Clicking during measurement cycle? ☒ Y/N		
Logger enclosure		Replaced (including everything inside)? ☒ Y/N New desiccant bags? ☒ Y/N		
Battery box		New box? ☒ Y/N New desiccant bags? ☒ Y/N		
Stakes		New one(s) drilled in? ☒ Y/N Length of new stake(s) 8 m? Y/N Bottom plugged to reduce melt-in? Y/N		
Tripod		New tripod? ☒ Y/N New sensor boom? ☒ Y/N		

with short cable exchanged
 → longer cable

minutes

Metadata maintenance


	Arrival	Departure
Time difference between logger clock and UTC ($\pm$ mm:ss)	03:30	0
Download data to PC and/or change CF Card (wait for green light)	(Y) N	Y / N
Name of logger program	— u —	Provice 2015e
Screen dump of values in fast scan mode	Y / (N)	(Y) / N
Photos of tripod, sensors, logger box wiring etc. (more is better)	(Y) N	(Y) / N
Mast tilt towards radiometer (- if tilting towards anemometer)	°	4 °
Mast tilt across boom looking from radiometer (- if clockwise)	°	1 °
Boom direction relative to north <i>see drawing</i>	° true/magn.	° true/magn.
Box on wind sensor exactly towards mast? If not, measure.	Y / N	(Y) / N
Radiometer exactly aligned with inclinometer? If not, measure.	Y / N	(Y) / N
Temperature / humidity height (bottom of casing – surface)	cm	184 cm
Stake assembly standing?	(Y) N / sort of	(Y) N / sort of
Free length of stake (if 3: outer, holding boom with sonic ranger)	cm	168 + 54 cm
Free length of stake 2 (if 3: middle)	cm	166 + 45 cm
Free length of stake 3 (if 3: outer, without sonic ranger)	cm	157 + 50 cm
Height of ablation bladder fluid level above the ice surface	cm	÷ cm
Vertical difference in surface height (at station – at hose) (approx.)	cm	÷ cm
Length of thermistor string on surface from surface marking	cm	÷ cm
Apparent damage to sensors? If yes, which?	Y / N	Y / (N)

to snow + 47 cm snow depth

Notes:

~~Ablation
13.6 m depth
from surface to ice
casing markings
at 1m long~~

stakes: $\left| \begin{array}{l} \text{to snow} \\ \text{surf} \end{array} \right| \neq \text{snow depth}$

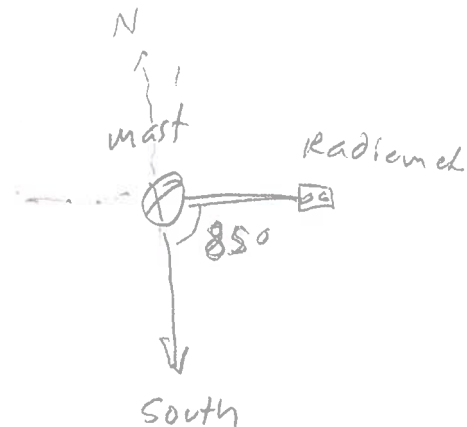

Must-do at next visit:
